


PACKAGING




*In this installation there are 3 or 4 critical points to evaluate:

1) Forming packages of 4 tiles, the tiles are not well aligned.

(They should be aligned as the bundle is being formed or when strapping).

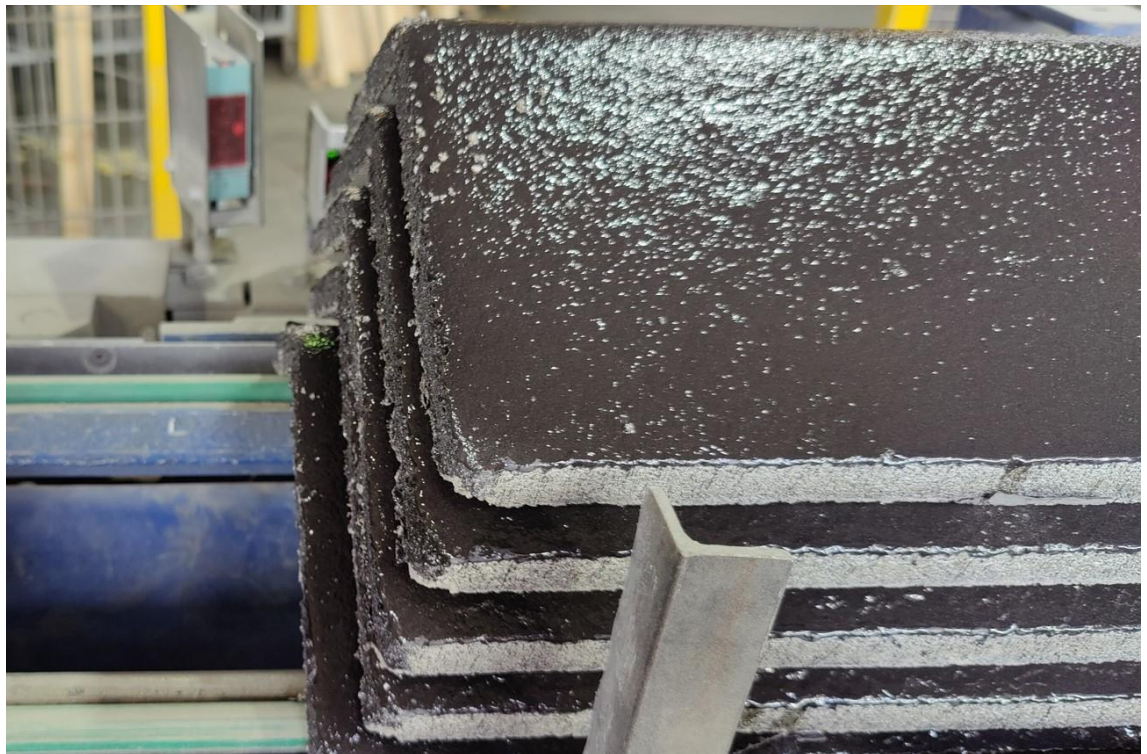

***See the possibility of aligning the tiles in the formation of the package.**

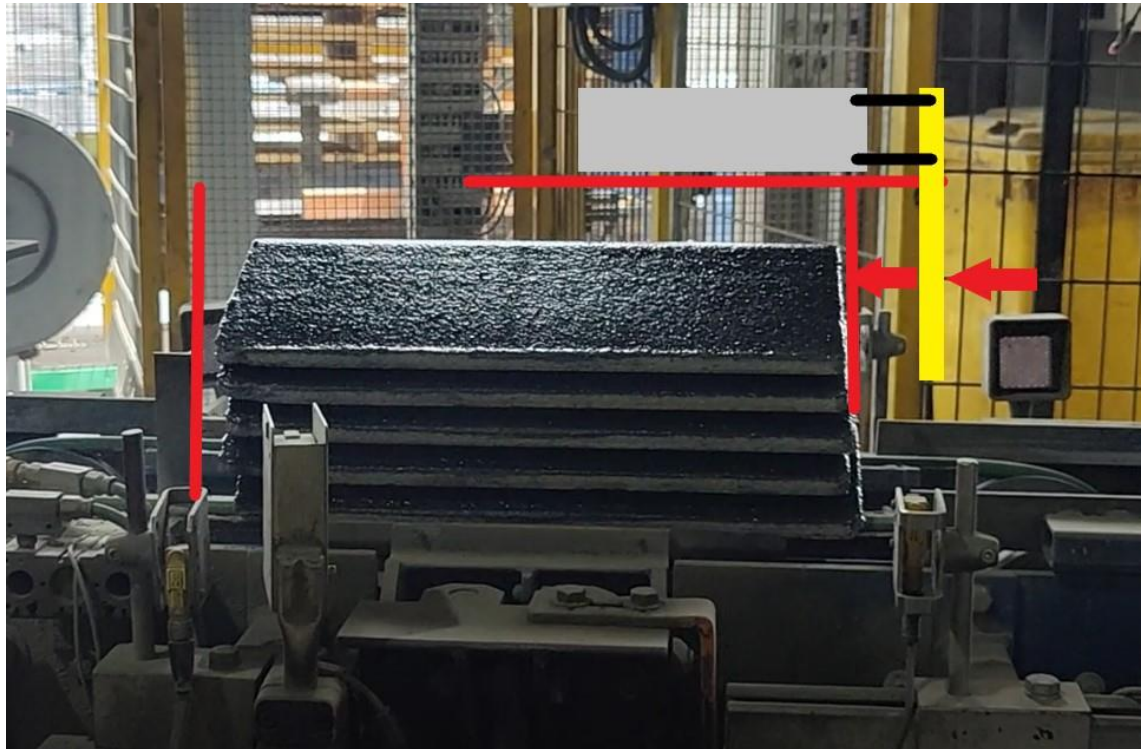

2)*When strapping the packages of 4 tiles, they do not fit well, the strap seems to me too rigid and does not fit, for the arch of the 4 tiles,

(Poorly fitted and poorly welded/not aligned).



***See the possibility of aligning the tiles in the strapping of the package.**



3) *When forming the bundle there is excessive slippage and shock at the base of the tiles, generating friction and loosening the bundle.

(When forming the bundle, if it is poorly welded or not tightened, the bundle becomes unstable).

(It would have to be placed from lower / lower height).



4)* When the packet is formed, there is free space between the packets, when they are left on the plastic base.

(You should help them to fit closer together as they are arranged).



4)* When placing the vertical bundles for horizontal strapping, the bundles are pushed backwards and tip over.

(The "most compact bundle" is formed or "the tiles must be followed up to the strapping position".)





THERMOSHRINKING

- 1) ***In the palletising of the RIDGE TILE, the strapping of the loose packages is identified, in my opinion for RIDGE TILE to have a better hold, the plastic bag should be closed and shrink-wrapped at the top, if it has excess moisture, with holes in the plastic, to avoid moisture inside the bag.**

